

Statesville Downtown Streetscape – Phase II




Statesville Downtown Streetscape – Phase II



Statesville Downtown Streetscape – Phase II

Construction Sequence

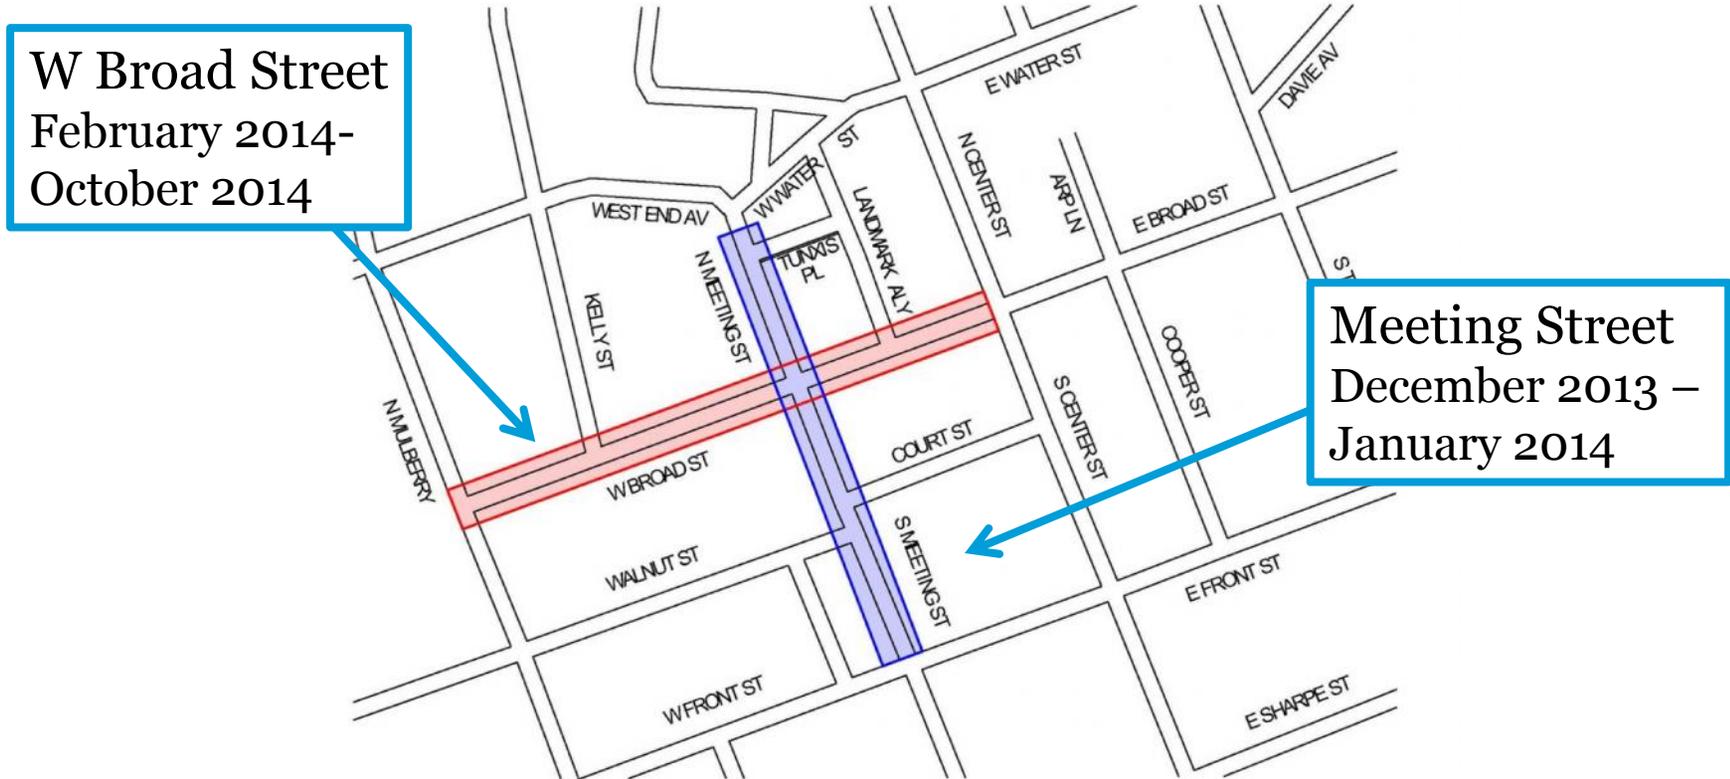



Statesville Downtown Streetscape – Phase II

Order of Construction:

Traffic Control and Demolition

Water Lines

Storm Drain

Electrical

Traffic Signals

Curb & Gutter

Sidewalk


Pavers

Furnishings, Landscaping & Decorative Lights

Street Paving

Statesville Downtown Streetscape – Phase II

Typical Work Zone

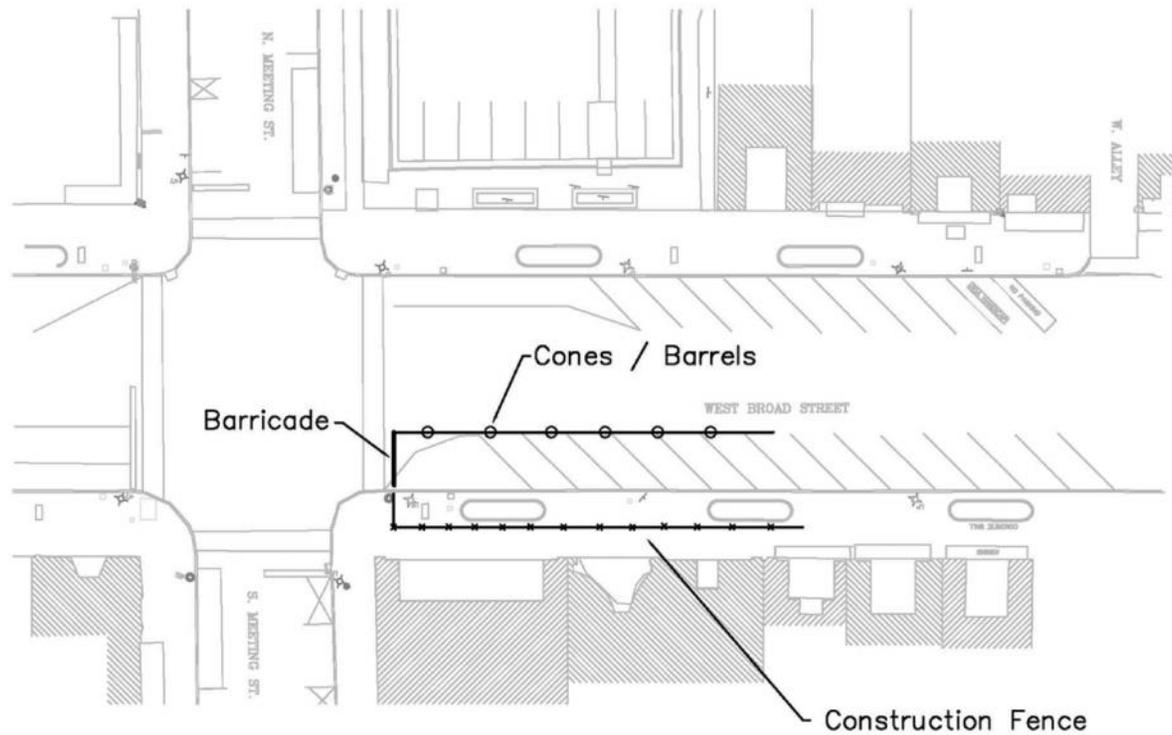



Statesville Downtown Streetscape – Phase II

Proposed Construction Schedule (Subject to Change)

Meeting Street:

Front to Broad

Dec, 2013 to Jan, 2014 (weather

Broad to Water

Dec, 2013 to Jan, 2014 dependent)

North side of W Broad Street:

Center to Kelly (water line only)

February, 2014

South side of W Broad Street:

Center to Meeting

March, 2014 – May, 2014

Meeting to Mulberry

April, 2014 – June, 2014

North side of W Broad Street:

Center to Meeting

June, 2014 – July, 2014

Meeting to Mulberry

July, 2014 – August, 2014

Final Paving and Completion

September, 2014 – October, 2014



Statesville Downtown Streetscape – Phase II

Contacts:

Brendon Pritchard, PE
Assistant City Engineer
bpritchard@statesvillenc.net
(704) 878-3552

www.ci.statesville.nc.us
